


STAGE IV-A

1. AFTER COMPLETION OF STAGE III-B, REMOVE REMAINDER OF CONCRETE TARMAC PAVEMENT AND TEMPORARY PAVEMENT.
2. NEW COMMISSARY TRUCK DOCK ACCESS DRIVE IS TO REMAIN TOTALLY FUNCTIONAL DURING CONSTRUCTION OF THE REMAINDER OF THE ACCESS DRIVE.

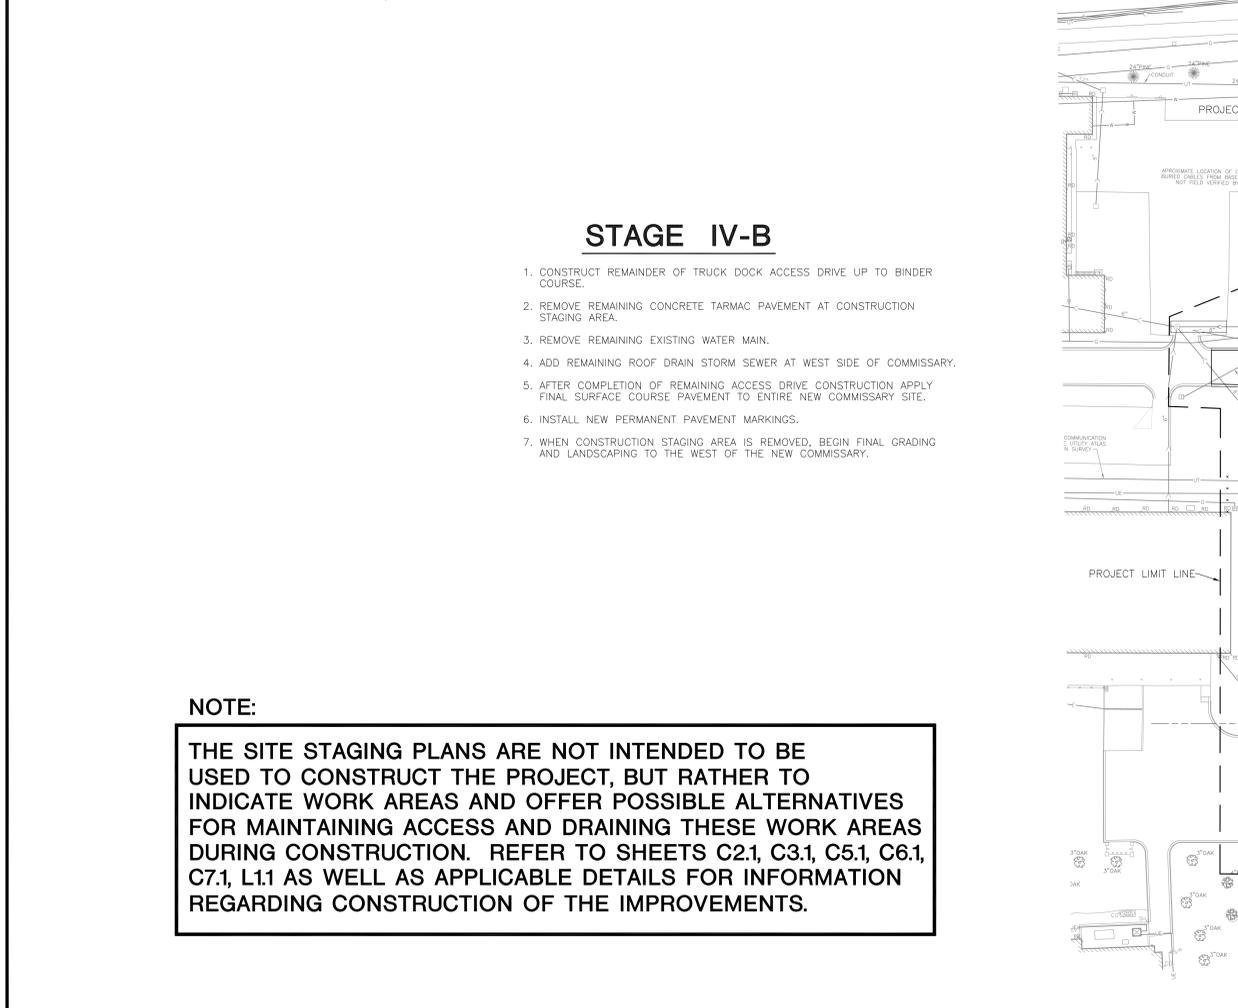


STAGE IV-B

1. CONSTRUCT REMAINDER OF TRUCK DOCK ACCESS DRIVE UP TO BINDER COURSE.
2. REMOVE REMAINING CONCRETE TARMAC PAVEMENT AT CONSTRUCTION STAGING AREA.
3. REMOVE REMAINING EXISTING WATER MAIN.
4. ADD REMAINING ROOF DRAIN STORM SEWER AT WEST SIDE OF COMMISSARY.
5. AFTER COMPLETION OF REMAINING ACCESS DRIVE CONSTRUCTION APPLY FINAL SURFACE COURSE PAVEMENT TO ENTIRE NEW COMMISSARY SITE.
6. INSTALL NEW PERMANENT PAVEMENT MARKINGS.
7. WHEN CONSTRUCTION STAGING AREA IS REMOVED, BEGIN FINAL GRADING AND LANDSCAPING TO THE WEST OF THE NEW COMMISSARY.

NOTE:

THE SITE STAGING PLANS ARE NOT INTENDED TO BE USED TO CONSTRUCT THE PROJECT, BUT RATHER TO INDICATE WORK AREAS AND OFFER POSSIBLE ALTERNATIVES FOR MAINTAINING ACCESS AND DRAINING THESE WORK AREAS DURING CONSTRUCTION. REFER TO SHEETS C2.1, C3.1, C5.1, C6.1, C7.1, L1.1 AS WELL AS APPLICABLE DETAILS FOR INFORMATION REGARDING CONSTRUCTION OF THE IMPROVEMENTS.

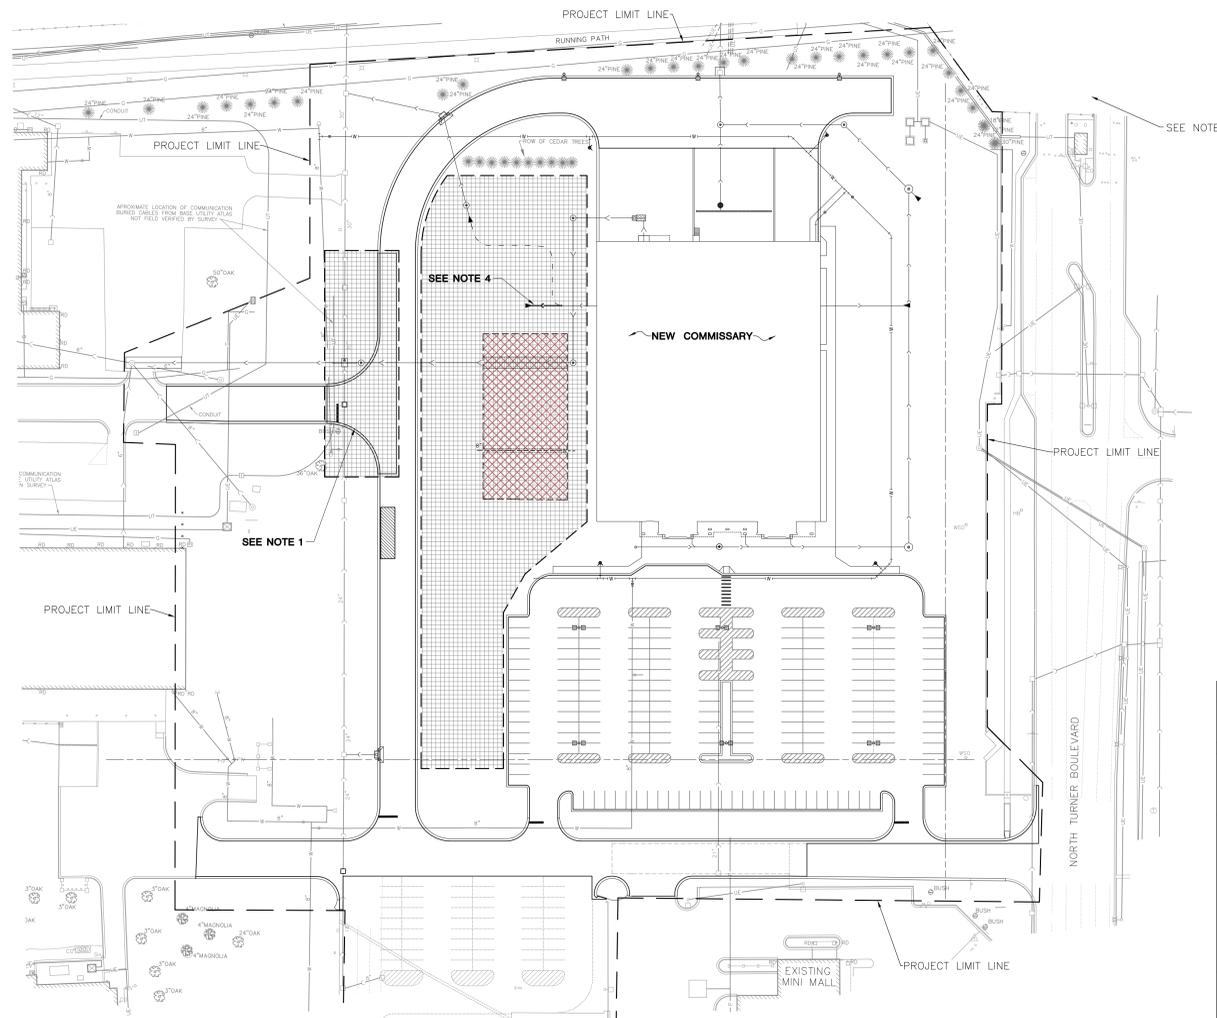

NOTES

1. CONSTRUCTION ACCESS TO THE PROJECT SITE WILL BE VIA THE DICKINSON GATE. THE DICKINSON GATE WILL BE UNDERGOING RENOVATION DURING THE COMMISSARY PROJECT. FOR PART OF THE PROJECT DURATION, CONSTRUCTION TRAFFIC WILL BE REQUIRED TO USE A TEMPORARY ACCESS GATE LOCATED DIRECTLY ADJACENT TO THE DICKINSON GATE. REFER TO ATTACHMENT 20 FOR PLANS OF THE DICKINSON GATE PROJECT.

LEGEND

- BITUMINOUS PAVEMENT REMOVAL
- CONCRETE TARMAC REMOVAL
- TEMPORARY BITUMINOUS PAVEMENT
- STAGE WORK AREA
- NEW GRAVEL CONSTRUCTION STAGING AREA
- TO BE REMOVED
- NEW ITEM TO BE CONSTRUCTED DURING CURRENT STAGE
- NEW ITEM CONSTRUCTED DURING PREVIOUS STAGE
- UTILITY TO BE REMOVED (SEE SHEET C2.1 FOR UTILITY LEGEND)

21 JUN 2012		AMENDMENT 0001	
SYM.	B.O. NO.	ACTION	DATE
			DESCRIPTION OF REVISION
 DEFENSE COMMISSARY AGENCY DeCA LOGISTICS AND ENGINEERING GROUP FORT LEE, VIRGINIA LACKLAND AFB, TEXAS			
DESIGNED BY:	DESIGN/BUILD NEW COMMISSARY SITE STAGING PLAN - STAGE IV MAXWELL A.F.B. - GUNTER ANNEX, ALABAMA		
DRAWN BY:			
REVIEWED BY:			
SUBMITTED BY:	SOL. NO.	HDEC03-12-R-0003	DATE: 21 JUN 2012
ENGINEER:	PROJECT NO.	DECA/PROB	SEQUENCE NO.
	DRAWING NUMBER	SHEET NO.	C2.5
