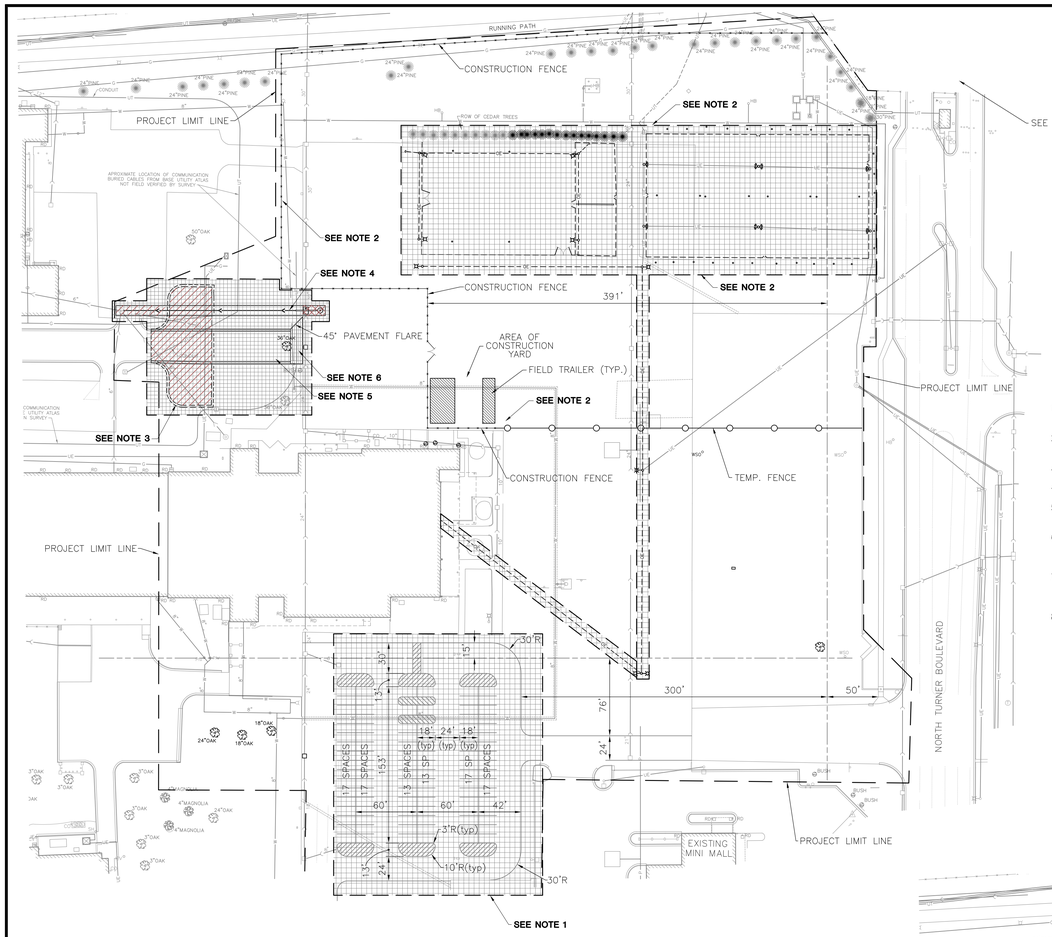

STAGE I-A

1. STRIPE NEW TEMPORARY PARKING AREA PAVEMENT MARKINGS AS SHOWN ON STAGE I–A PLAN.
2. BEGIN TO SET UP CONSTRUCTION FENCE, TEMP FENCE AND CONSTRUCTION YARD AT THE NORTHEAST CORNER OF EXISTING COMMISSARY.
3. REMOVE EXISTING BITUMINOUS PAVEMENT AND CONCRETE CURB AND GUTTER.
4. CONSTRUCT NEW SANITARY SEWER ALONG WITH INTERFERENCE BOX AND MANHOLE.
5. CONSTRUCT NEW PAVEMENT AND CONCRETE CURB AND GUTTER TO BEGINNING OF RADIUS RETURN.
6. ADD TEMPORARY BITUMINOUS PAVEMENT BETWEEN NEW PAVEMENT AND EXISTING CONCRETE TARMAC PAVEMENT. MATCH ELEVATION OF NEW AND EXISTING PAVEMENTS.
7. REMOVE ALL ABOVE GROUND EXISTING TOPO FEATURE. (FENCES, POWER POLES, LIGHT POLES, OVERHEAD ELECTRIC AND TREES. LEAVE FIRE HYDRANTS OR OTHER WATER APPURTANANCES IN PLACE UNTIL AFTER PAVEMENT REMOVAL.
8. EXISTING COMMISSARY TO REMAIN OPEN AND TOTALLY FUNCTIONAL AT ALL TIMES.

NORTH

GRAPHIC SCALE

(IN FEET)
1 inch = 60 ft.

NOTES

1. CONSTRUCTION ACCESS TO THE PROJECT SITE WILL BE VIA THE DICKINSON GATE. THE DICKINSON GATE WILL BE UNDERGOING RENOVATION DURING THE COMMISSARY PROJECT. FOR PART OF THE PROJECT DURATION, CONSTRUCTION TRAFFIC WILL BE REQUIRED TO USE A TEMPORARY ACCESS GATE LOCATED DIRECTLY ADJACENT TO THE DICKINSON GATE. REFER TO ATTACHMENT 20 FOR PLANS OF THE DICKINSON GATE PROJECT.

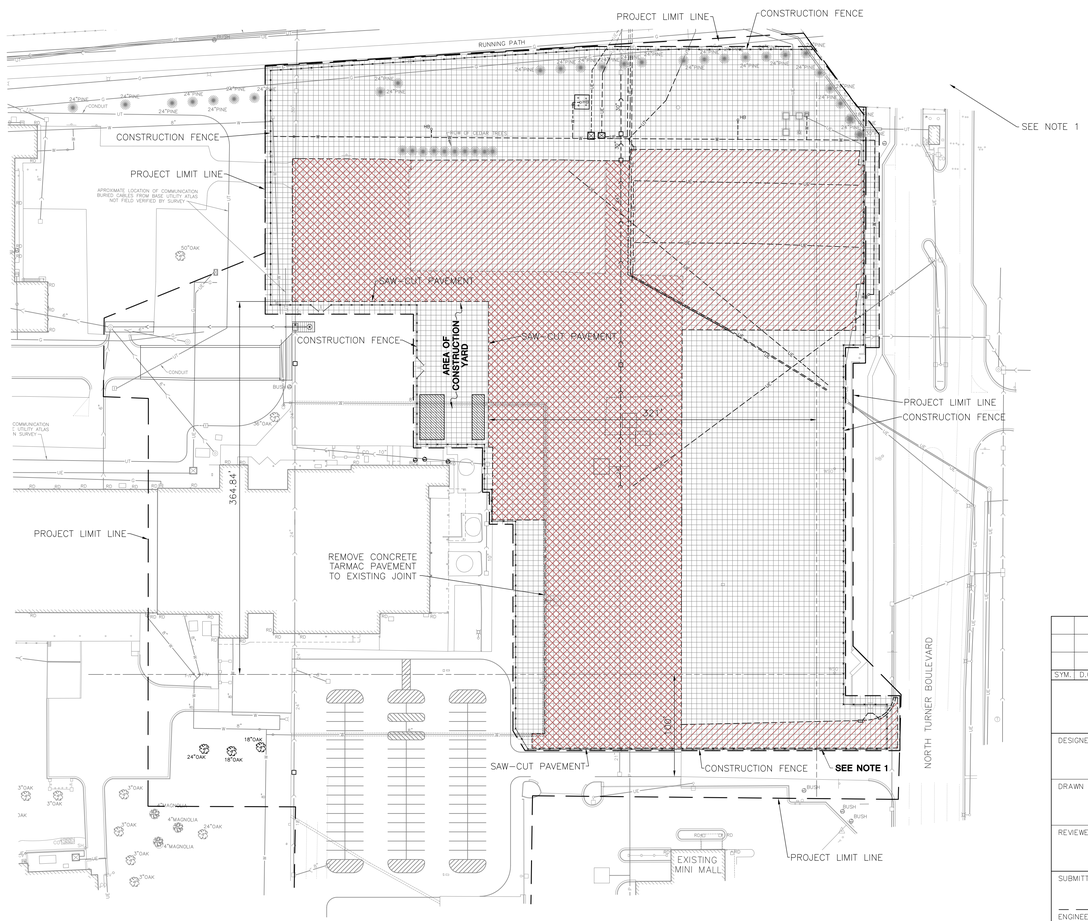

STAGE I-B

1. COMPLETE SET UP OF CONSTRUCTION FENCE AROUND REMAINING WORK AREA.
2. REMOVE EXISTING CONCRETE TARMAC AND BITUMINOUS PAVEMENT.
3. REMOVE EXISTING UNDERGROUND UTILITIES AS SHOWN. MAINTAIN SERVICE TO ALL SURROUNDING BUILDINGS AND USES AT ALL TIMES.

LEGEND

- BITUMINOUS PAVEMENT REMOVAL
- CONCRETE TARMAC REMOVAL
- TEMPORARY BITUMINOUS PAVEMENT
- STAGE WORK AREA
- TO BE REMOVED
- NEW ITEM TO BE CONSTRUCTED DURING CURRENT STAGE
- NEW ITEM CONSTRUCTED DURING PREVIOUS STAGE
- ---OE--- UTILITY TO BE REMOVED (SEE SHEET C2.1 FOR UTILITY LEGEND)
- CONSTRUCTION FENCE
- NEW SANITARY SEWER

NOTE:

THE SITE STAGING PLANS ARE NOT INTENDED TO BE USED TO CONSTRUCT THE PROJECT, BUT RATHER TO INDICATE WORK AREAS AND OFFER POSSIBLE ALTERNATIVES FOR MAINTAINING ACCESS AND DRAINING THESE WORK AREAS DURING CONSTRUCTION. REFER TO SHEETS C2.1, C3.1, C5.1, C6.1, C7.1, L1.1 AS WELL AS APPLICABLE DETAILS FOR INFORMATION REGARDING CONSTRUCTION OF THE IMPROVEMENTS.

SYM.	D.O. NO.	ACTION	DATE	DESCRIPTION OF REVISION
			27 JUN 2012	AMENDMENT 0001

DEFENSE COMMISSARY AGENCY
DeCA LOGISTICS AND ENGINEERING GROUP
FORT LEE, VIRGINIA
LACKLAND AFB, TEXAS

DESIGNED BY:
DRAWN BY:
REVIEWED BY:
SUBMITTED BY:
ENGINEER:

DESIGN/BUILD NEW COMMISSARY

SITE STAGING PLAN - STAGE I

MAXWELL A.F.B. – GUNTER ANNEX, ALABAMA

SOL. NO. HDEC03-12-R-0003 | DATE: 27 JUN 2012
PROJECT NO. DEC4MP05
DRAWING NUMBER | SHEET NO. OF | SEQUENCE NO. C2.2
